


2018.03
EXIT 44 SOUTHBOUND ON RAMP IMPROVEMENTS
MILE 44.3
Project Update
March 15, 2018

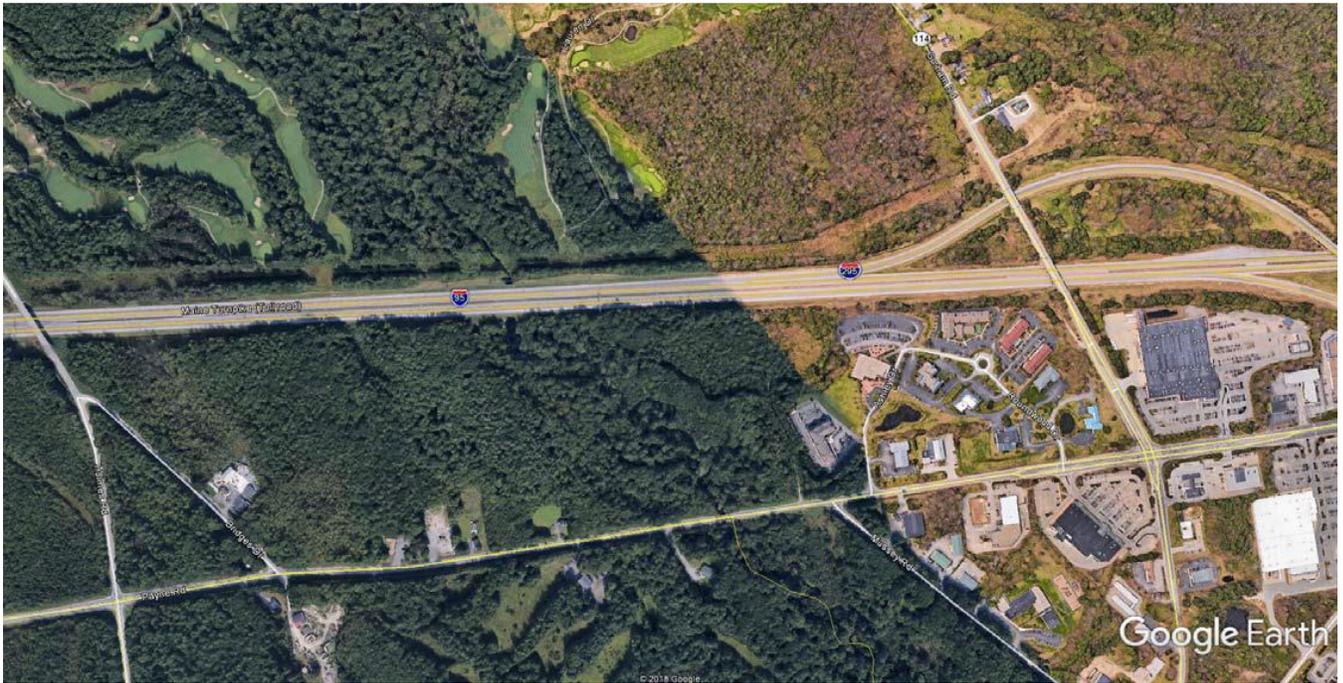

Contractor: R.J. Grondin & Sons **Bid Amount:** \$1,436,720
Percent Complete last approved pay estimate: 0%

Project Schedule: Completion date November 27, 2018.
Substantial Completion June 21, 2018

Project Scope: The roadway work consists of improving the southbound on ramp at Exit 44 in the Town of Scarborough, Maine. The existing one lane entrance ramp will be widened to accommodate a two lane parallel entrance ramp merging with the two existing mainline travel lanes. The work includes reconstruction and grading on the mainline and ramp with earthwork, pavement, maintenance of traffic, signing, striping, guardrail, and electrical work. Substantial completion is having the work complete except for punchlist items and grass growth.

Contractor Schedule: RJ Grondin and Sons will begin mobilizing on site installing traffic control signs. They are planning to shift travel lanes the week of March 25th. The travel lanes will be shifted to the left to allow for temporary concrete barrier to be set along the shoulder to provide a positive barrier between the traffic and the work zone.
