


2018.15
Cobbosseecontee Stream Bridge Rehabilitation
Androscoggin River Bridge Repair
April 22, 2019

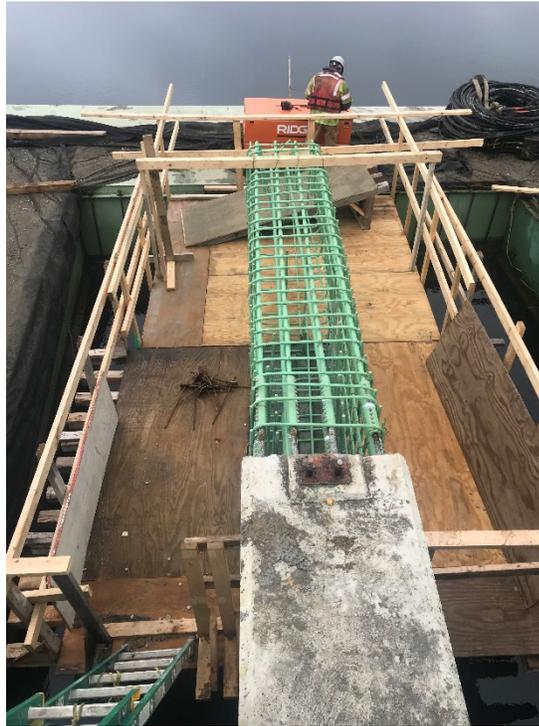

Pier two cap extension rebar

Contractor: Wyman & Simpson Inc.

Bid Amount: \$ \$6,784,907

Percent Complete last approved pay estimate: 24%

Project Schedule: Completion date June 4, 2021

Project Scope: The work consists of rehabilitating the Cobbosseecontee Stream Overpass (NB & SB) bridge in the Town of Litchfield/West Gardiner, Maine and repairing the Androscoggin River Overpass (NB & SB) bridges in the City of Lewiston/Town of Auburn, Maine. The work includes concrete deck and steel girder placement, concrete substructure modifications and repairs, approach work and paving, guardrail, bridge rails, substructure concrete repairs, bearing repairs, post tensioning sleeve repairs, maintenance of traffic, and all other work incidental thereto in accordance with the Plans and Specifications.

Contractor Schedule: At Cobbosseecontee, Wyman & Simpson completed the pier extension work at Pier 1 and 2, they should have pier 3 completed in the next week. Over the next several weeks they are planning to sawcut and remove the bridge deck and begin work on abutment one extension.

At the Androscoggin River, Wyman & Simpson will be replacing a bridge bearing under the northbound bridge. They are also mobilizing on site to resume the bridge repair at Abutment 1.
