


2019.09
Bridge Improvements Stroudwater River Overpass Mile 46.7
& Maine Central Railroad Overpass Mile 47.9
Project Update
November 19, 2019

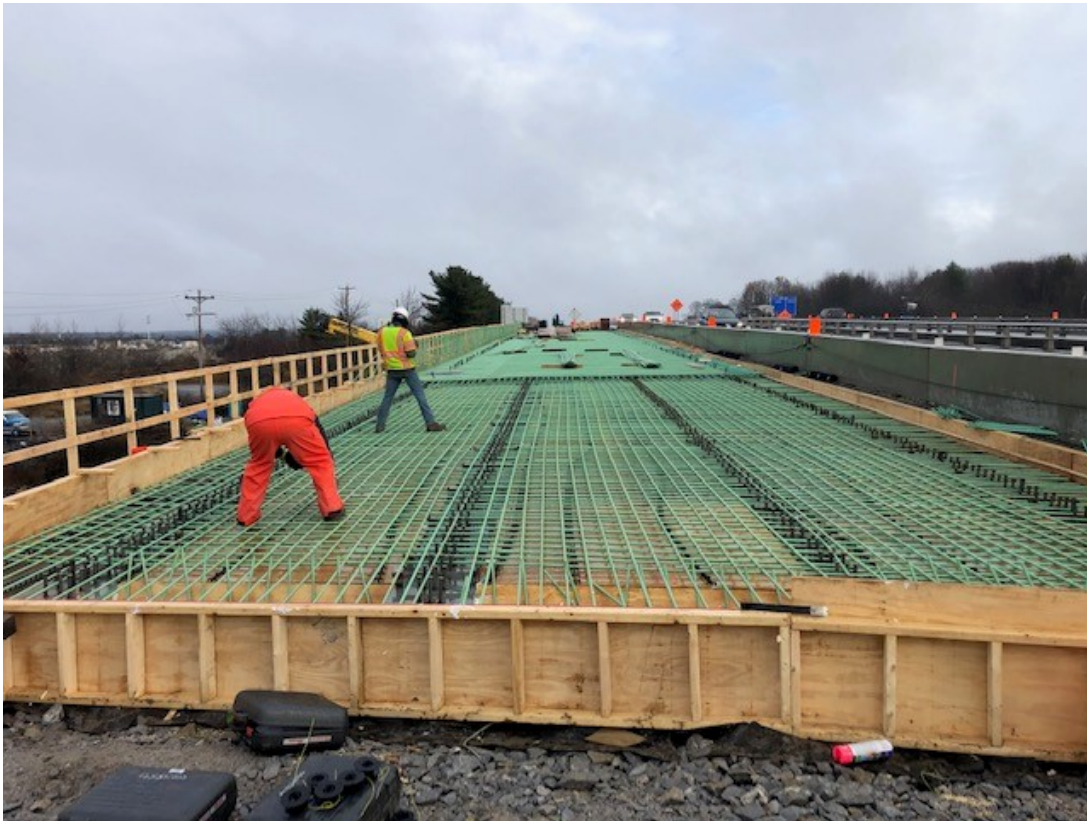

Placing rebar prior to deck placement planned for next week southbound at MCRR

Contractor: Cianbro

Bid Amount: \$20,460,607.50

Percent Complete last approved pay estimate: 47.3%

Project Schedule: Completion date June 25, 2021.

Project Scope: The work consists of improving the Stroudwater River Overpass (NB & SB) bridges and Maine Central Railroad Overpass (NB & SB) bridges in the City of Portland, Maine. The work includes phased construction, concrete deck and steel girder placement, concrete substructure modifications and repairs, approach work and paving, guardrail, bridge rails, substructure concrete repairs, bearing repairs, and maintenance of traffic.

Contractor Schedule: Work at Stroudwater – The contractor is looking to set structural steel next week for the NB bridge. They continue to work on the sub structure, focusing on pier 2 and abutment 1.

Work at MCRR – The contractor placed the NB deck last week and it is currently curing. They will start on the parapet walls in the next week. Crews are placing and tying rebar and building formwork for the SB bridge deck and hope to place this sometime next week.
