
2022.07 Saco Interchange Improvements May 23, 2025

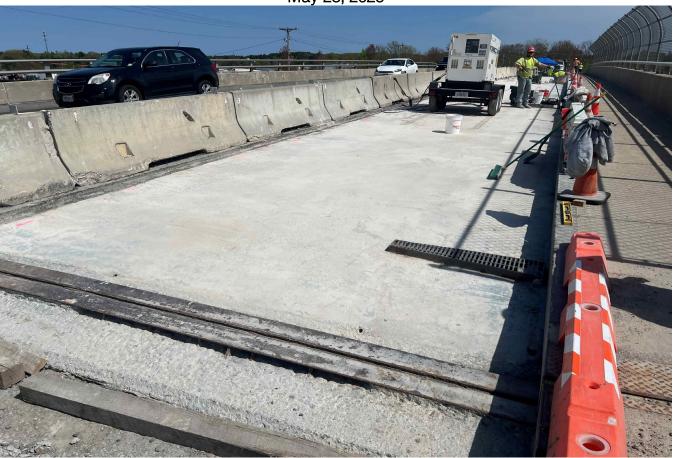

Looking east at the Route 112 Bridge in Saco where the contractor is making repairs to the deck and joints

Contractor: Sargent Corporation Bid Amount: \$41,922,810.00

Percent Complete last approved pay estimate: 80.1 %

Project Schedule: Completion date November 21, 2025

Project Scope: The work consists of highway, interchange, and toll system construction at Exit 35 in Saco and modifications to the Exit 36 Interchange in Saco. The work includes a new interchange at MM 35, including southbound and northbound ramps, earthwork, pavement, concrete, signing, overhead sign structures, concrete barrier, guardrail, drainage, stormwater management, electrical work, highway lighting, lightning suppression systems, and maintenance of traffic.

Contractor Schedule: Along mainline, crews are working in the right northbound shoulder, forming a sign bridge foundation. On Route 112, the contractor is installing new drainage and rebuilding the adjacent sidewalk at the southbound interchange. They are also performing concrete and joint repairs along the south side of the bridge. At the northbound plaza, crews are installing sensor loops and performing various electrical terminations at the plazas.
