


2018.15
Cobbosseecontee Stream Bridge Rehabilitation
Androscoggin River Bridge Repair
January 17, 2020

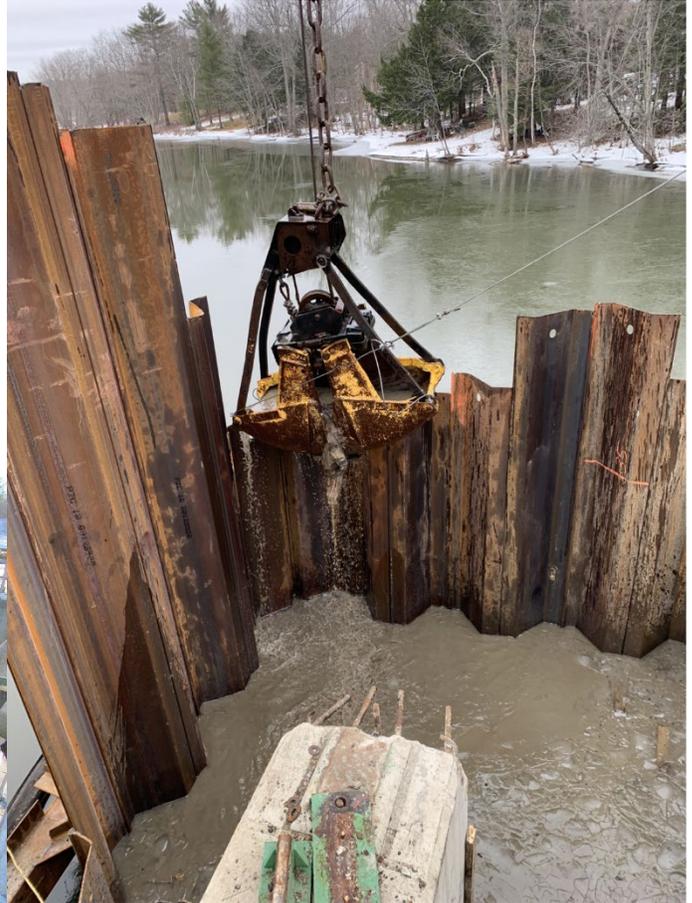

Excavating Cofferdams Airlifting (left photo), Clamshell bucket (right photo).

Contractor: Wyman & Simpson Inc.

Bid Amount: \$ \$6,784,907

Percent Complete last approved pay estimate: 75%

Project Schedule: Completion date June 4, 2021

Project Scope: The work consists of rehabilitating the Cobbosseecontee Stream Overpass (NB & SB) bridge in the Town of Litchfield/West Gardiner, Maine and repairing the Androscoggin River Overpass (NB & SB) bridges in the City of Lewiston/Town of Auburn, Maine. The work includes concrete deck and steel girder placement, concrete substructure modifications and repairs, approach work and paving, guardrail, bridge rails, substructure concrete repairs, bearing repairs, post tensioning sleeve repairs, maintenance of traffic, and all other work incidental thereto in accordance with the Plans and Specifications.

Contractor Schedule: At Cobbosseecontee: Wyman & Simpson have been working on the new pier extension for the new girder. They have installed the cofferdams at all three pier locations and are currently excavating at pier 1 and 3. Pier 2 has been excavated, seal concrete placed and dewatered.
