


**2017.03
Maxwell Rd Bridge
Project Update
August 28, 2017**

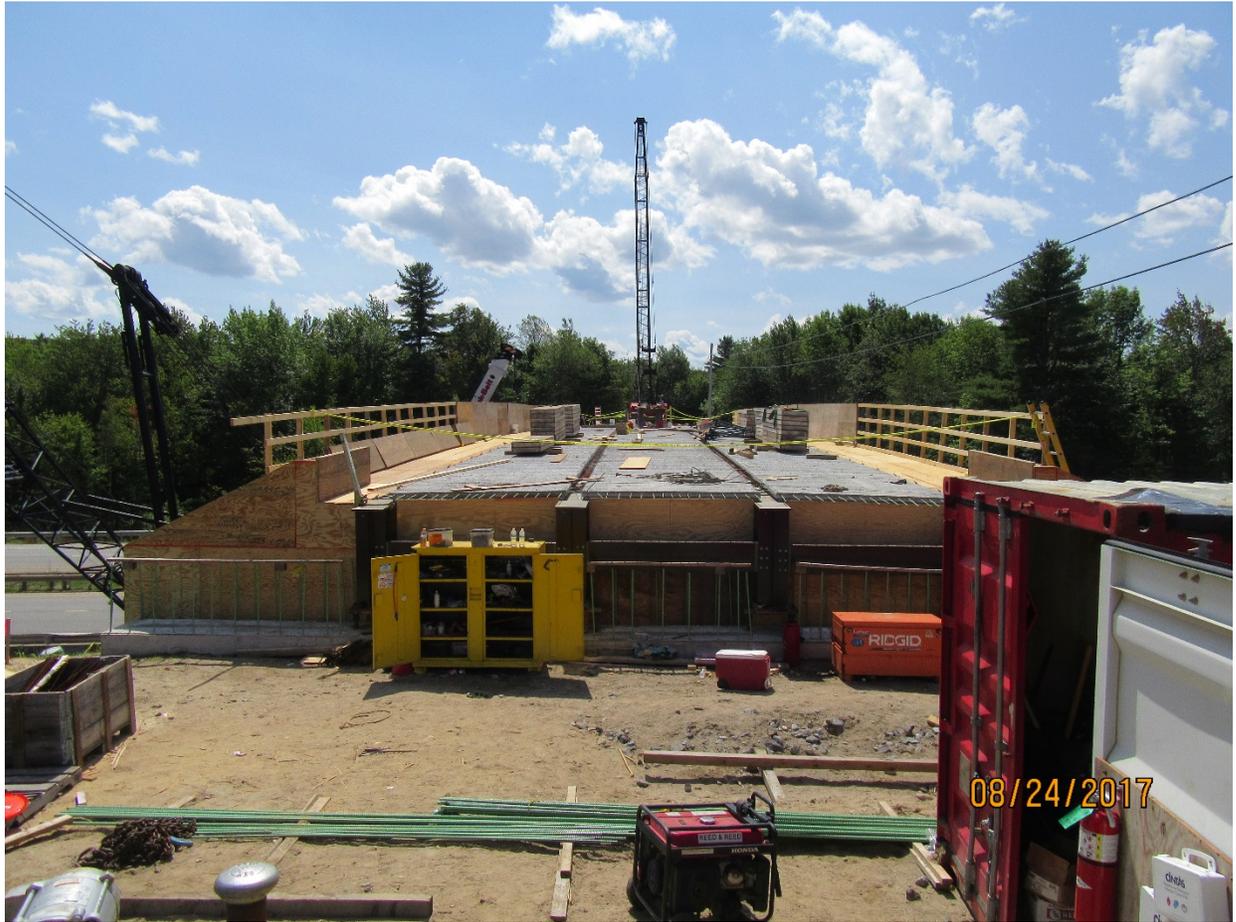

Contractor: Reed & Reed, Inc.

Bid Amount: \$ 1,796,866.00

Percent Complete last approved pay estimate: 64%

Project Schedule: Substantially complete by November 17, 2017

Project Scope: The Project consists of highway and bridge work required to replace the existing one lane Maxwell Road bridge over the Maine Turnpike in the Town of Sabattus, Maine. The work includes clearing, grading, drainage, base, pavement, guardrail, structural concrete, concrete deck, fabrication and erection of steel beams, steel bridge rails, and maintenance of traffic.

Contractor Schedule: Reed & Reed is working on forming the deck overhang and back walls, they are planning to place the new deck the second week of September. The schedule for this project has slipped several weeks but they are still anticipating to re-open the bridge by November 3rd, 7 months after they closed the bridge.
